



 COLLABORATE Share knowledge and drive outcomes	 BUILD RELIABLE Design resilient data systems	 DELIVER VALUE Enable data-driven decisions	 SECURE & GOVERN Protect data and ensure compliance
--	---	---	---

BI / DE Triage Operating Model

-  Operating Baseline (6 Month View Data Window)
-  RACI (Governance & Role Clarity)
-  Triage Working Checklist
-  Implementation Roadmap

6 Month - Operating Baseline

What BI and DE absorb in a typical two-week cycle

Operating baseline by Team

Team	Recent 6-Month Total	Avg per 2 Weeks	Enhancement per 2 Weeks	Support per 2 Weeks	Bug per 2 Weeks
BI	442	34.00	18.00	13.23	2.0
DE	515	39.62	36.85	2.08	0.69


6 Months - BI Combined Workload Distribution

Jira + Halo, normalized to a 2-week operating view

BI Combined (Jira + Halo) - Distribution of Work by Priority and Category

Work Category	Expedited	High	Highest	Medium	Low
Bug	4.8%	1.1%	0.2%	0.5%	1.6%
Enhancement / Product Feature	2.7%	8.1%	7.0%	12.4%	22.6%
Support	1.4%	1.6%	0.5%	31.9%	3.6%

BI Work Category Mix

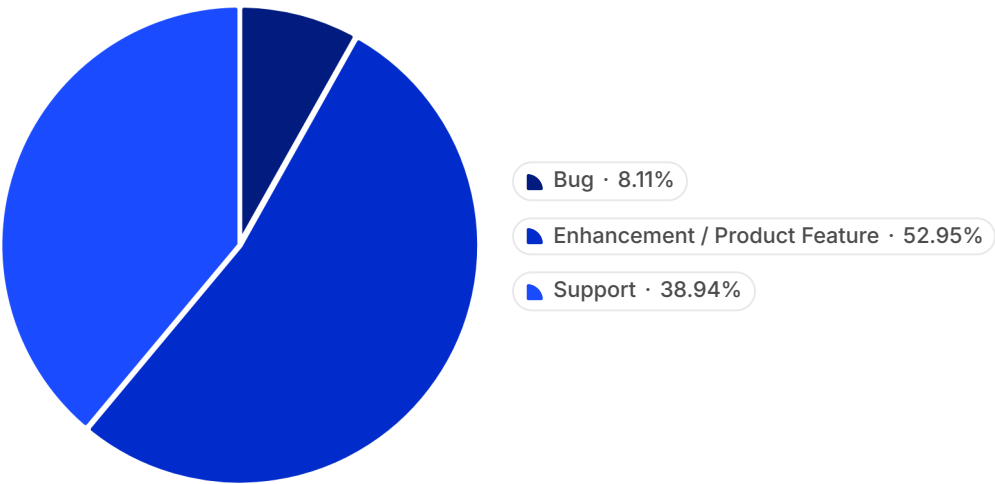


6 Months - DE Combined Workload Distribution

Jira + Halo, normalized to a 2-week operating view

DE Combined (Jira + Halo) - Priority Distribution Within Each Work Category, Avg per 2 Weeks

Work Category	Expedited	High	Highest	Medium	Low
Bug	0.4%	0.2%	0.0%	0.2%	1.0%
Enhancement / Product Feature	3.3%	19.8%	6.4%	21.7%	41.7%
Support	0.0%	0.0%	0.0%	5.2%	0.0%

DE Work Category Mix

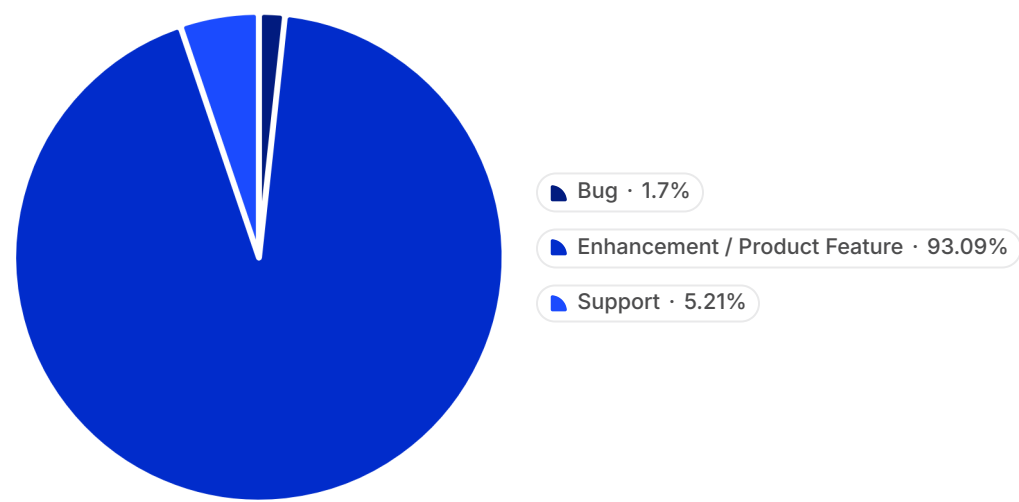

Suggested - 1st RACI: Intake, Readiness, and Planning Responsibilities

Role clarity for upstream BI / DE intake, triage, readiness, prioritization, and planning

Activity	CTO	Data Ops Manager	Product Manager	Scrum Master	Technical Lead <i>(Data Arch)</i>	Pod Team BI + DE	DQ / AI
Intake capture	I	A	R	C	I	C	I
Triage and classify	I	A/R	C	C	C	R	I
Product / Epic assignment	I	C	A/R	C	C	C	I
Enhancement value prioritization	C	C	A/R	C	C	C	I
Solution / data architecture review	I	C	C	I	A/R	R	C
Backlog refinement and grooming	I	C	A/R	R	C	R	C
Definition of Readiness check	I	C	A	R	C	R	C
Pointing / estimation	I	I	C	R	C	A/R	C
Support / Bug rotation coordination	I	A/R	I	C	C	R	I
Capacity view / sprint availability	I	A	C	R	C	R	I
Enhancement recommendation / candidate selection	I	C	A/R	C	C	C	I
Low / Medium enhancement filtering	I	C	A/R	C	C	C	I
2-week commitment planning	I	A	R	R	C	R	R

 **Product Manager** owns value, priority, backlog intent, and readiness of backlog content. **Data Ops Manager** owns triage governance, capacity discipline, and operating health. **Scrum Master** facilitates cadence, refinement, readiness checks, sprint capacity visibility, flow, and blockers. **Pod Team BI + DE** owns estimation and delivery feasibility.

Suggested - 2nd RACI: Execution, Validation, Metrics, and Tuning Responsibilities

Clarifying roles for successful delivery, monitoring, and continuous improvement in the BI / DE workflow.

Activity	CTO	Data Ops Manager	Product Manager	Scrum Master	Technical Lead <i>(Data Arch)</i>	Pod Team BI + DE	DQ / AI
Execution of Support / Bug / Enhancement work	I	I	I	C	C	A/R	C
Critical defect / restore coordination	C	A/R	I	C	C	R	C
Validation and acceptance if needed	I	C	A	C	C	R	C
Metrics review and tuning feedback	I	R	C	A/R	C	C	C
Product Roadmap Commitment	A	C	R	I	C	C	I
Operating model improvement and tuning	I	A	C	R	C	C	C


Legend:

- A = Accountable
- R = Responsible
- C = Consulted
- I = Informed
- A/R = Accountable and Responsible

CTO is accountable for Product Roadmap Commitment in line with business direction. **Data Ops Manager** owns execution governance, restore coordination, metrics review, and operating-model tuning. **Scrum Master** supports flow, blockers, metrics cadence, and improvement feedback loops. **Pod Team BI + DE** owns technical execution and delivery reality.

BI / DE Triage Working Checklist

What must be checked before work moves through the triage flow

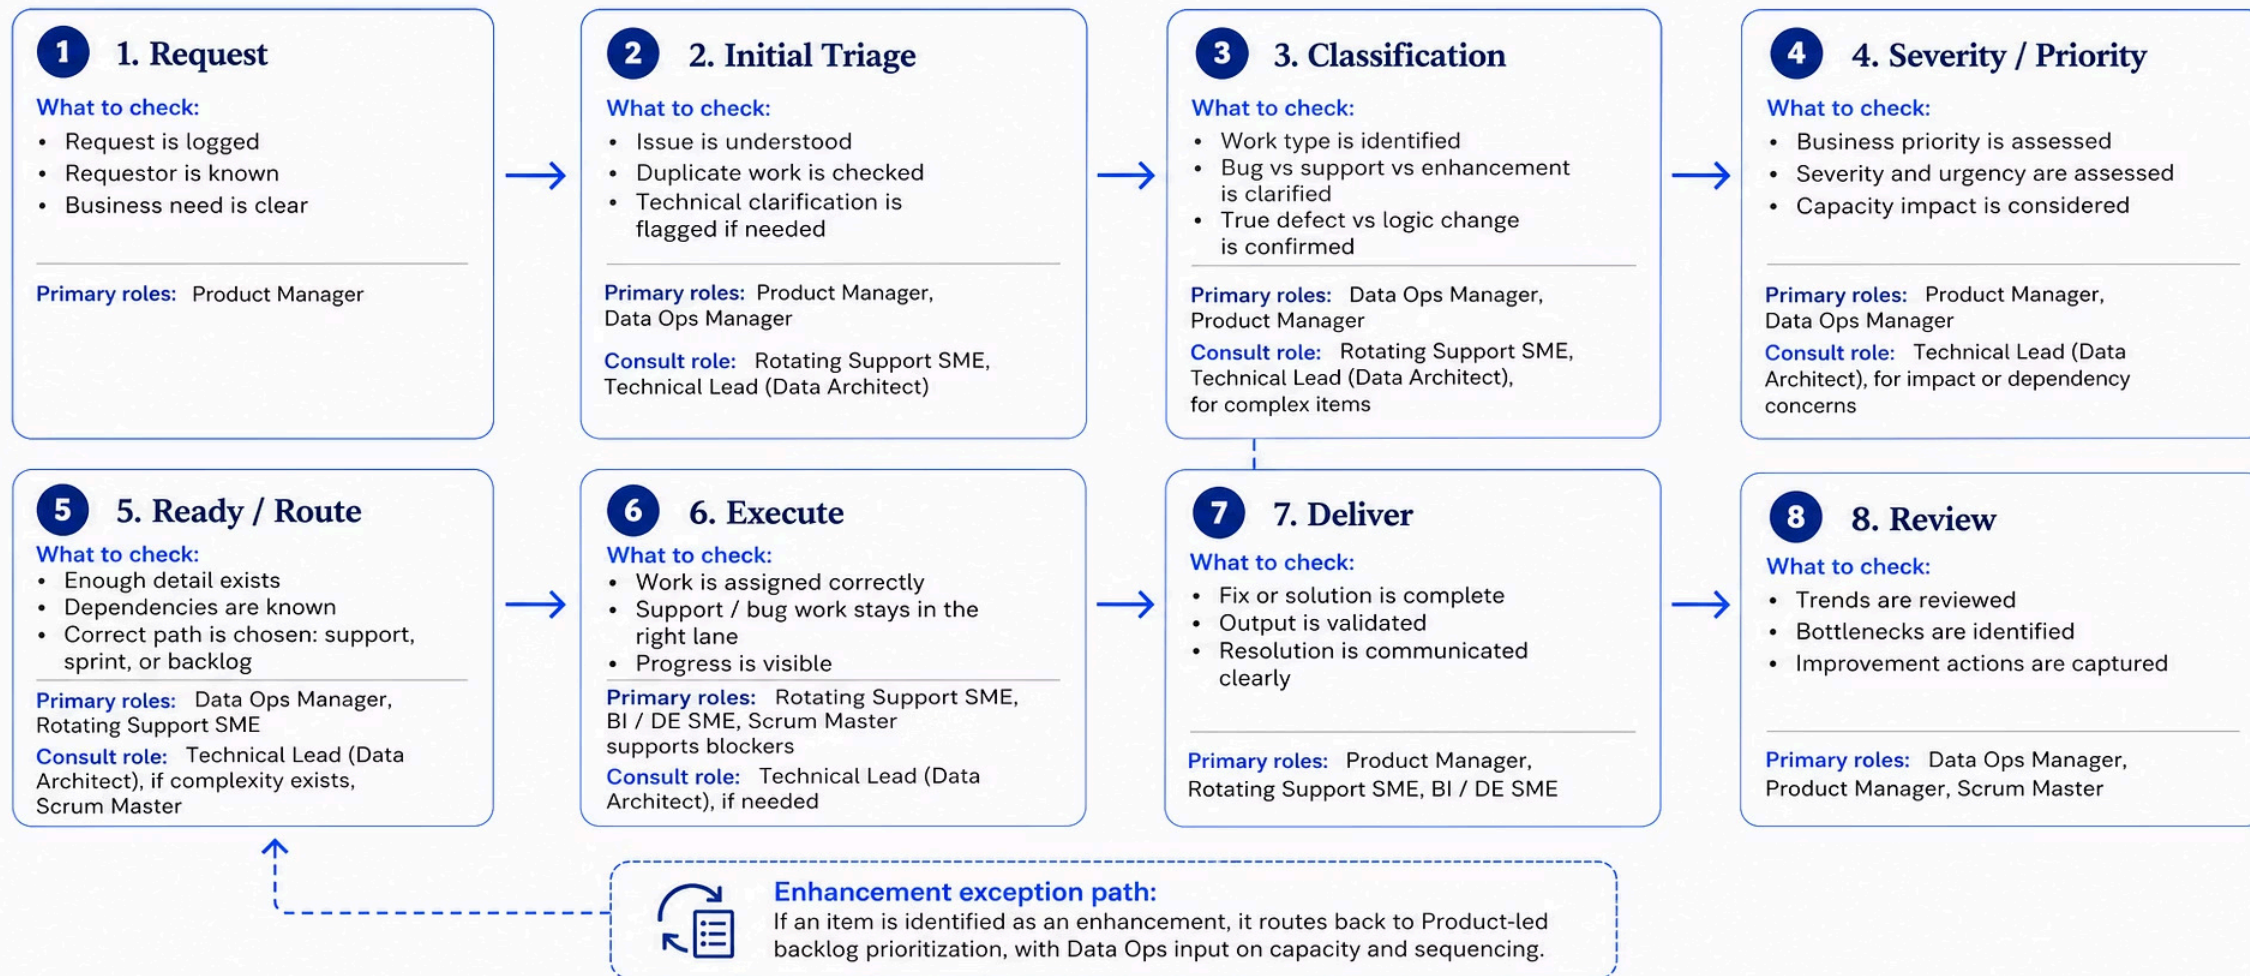


Triage is facilitated by the Data Ops Manager, informed by Product, and operationally supported by the Rotating Support SME.



Current-state note: Until a Technical Lead (Data Architect) role is established, selected technical triage support may be provided by BI / DE SMEs.

Suggested Operating Cadence

A simple cadence to run BI / DE triage consistently and effectively.

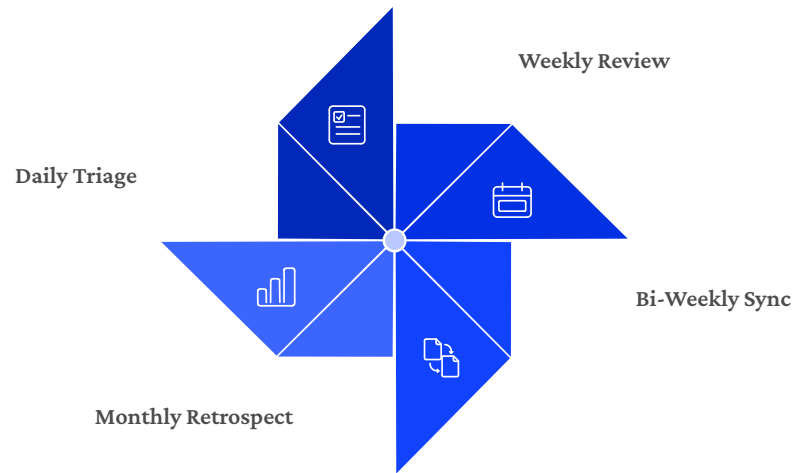

Daily / 3x Weekly Support Triage

Review new issues and assign ownership promptly.



Weekly Enhancement Readiness Review

Check scope, readiness, and dependencies for future work.



Bi-Weekly Sprint Planning & Capacity Review

Confirm commitments and available team capacity.



Monthly Metrics Review

Analyze trends, identify bottlenecks, and plan improvements.

Execution Roadmap

A phased rollout to align, configure, launch, and tune the BI / DE triage operating model.

1 Sign Off

Confirm agreement on the model, RACI, checklist, and rollout direction.

2 Design

Finalize process, roles, intake rules, board structure, workflows, and KPIs.

3 Board & KPI Setup

Configure MMSP / ALC pod boards, triage fields, workflows, and reporting views.

4 Go Live

Use the new process for intake, support / bugs, enhancement routing, and sprint planning.

5 Continuous Optimization

Review metrics monthly, refine rules, and tune the operating model.

SUMMARY

Thank You


Aligning on the Scrumban operating model and next steps



What We Aligned On



What We Need to Decide

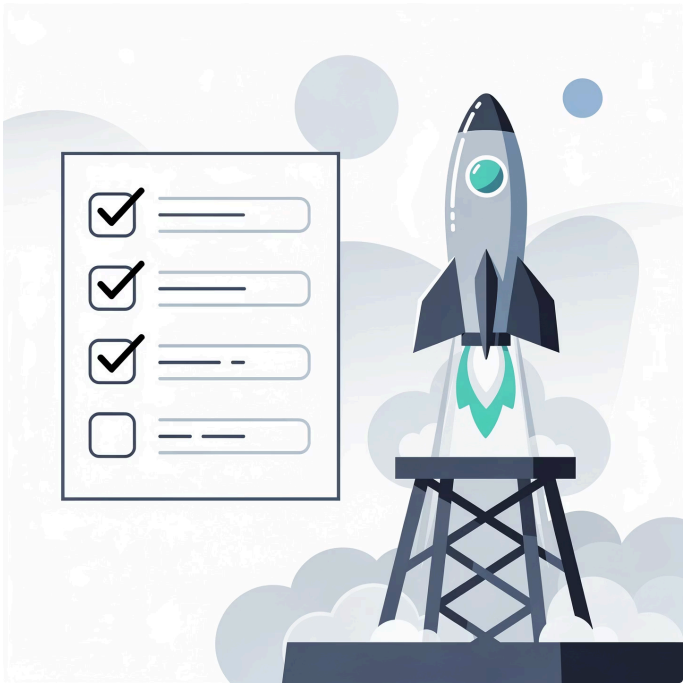

Recommended Next Steps
